Project Planning Phase

Project Planning Template (Product Backlog, Sprint Planning, Stories, Story Points)

Date	14 October 2026
Team ID	———————————————
Project Name	Car Rental Request Automation in ServiceNow Using Service Catalog and Workflows
Maximum Marks	5 Marks

Product Backlog, Sprint Schedule and Estimation (4 Marks)

Below are the product backlog and sprint schedule for the Car Rental Request Automation project: 26 user stories across 6 epics, estimated in story points of 1, 2, 3 and 5.

Sprint	Functional requirement (epic)	User story no.	User story / task	Story points	Priority	Team member
Sprint-1	Requirement analysis & planning	USN-1	As a project owner, I can set out the business goals for automating car rental requests.	2	High	Vamsi Bhavirisetti
Sprint-1		USN-2	As a project owner, I can define the functional scope: catalog item, form, approvals, tasks, notifications and SLA.	2	High	Vamsi Bhavirisetti
Sprint-1		USN-3	As a project owner, I can identify the stakeholders (requesters, managers, transport team, admins) and what each needs.	1	Medium	Vamsi Bhavirisetti
Sprint-1		USN-4	As a project owner, I can draw up an execution roadmap with milestones for every phase.	1	Medium	Vamsi Bhavirisetti
Sprint-1	Backend development & configuration (data architecture)	USN-5	As an admin, I can create an Update Set that tracks every configuration change for deployment.	1	High	Vamsi Bhavirisetti
Sprint-1		USN-6	As an admin, I can design the data architecture covering REQ, RITM, SCTASK, approvals and the Car Inventory table.	3	High	Vamsi Bhavirisetti
Sprint-1		USN-7	As an employee, I can use a “Car Rental Request” catalog item with variables for requested date, pick-up location, drop location, duration, car type and reason.	3	High	Vamsi Bhavirisetti
Sprint-1		USN-8	As an admin, I can set up Business Rules that assign tasks automatically and update the request status after approvals.	3	High	Vamsi Bhavirisetti
Sprint-2		USN-9	As a manager, I get an approval request from the flow (primary manager approval) whenever a car rental request is submitted.	3	High	Vamsi Bhavirisetti
Sprint-2		USN-10	As an approver, I can give the secondary car request approval once the flow has checked car availability.	3	High	Vamsi Bhavirisetti
Sprint-2		USN-11	As a transport team member, I get an assignment task (SCTASK) for each approved request.	2	High	Vamsi Bhavirisetti

Sprint	Functional requirement (epic)	User story no.	User story / task	Story points	Priority	Team member
Sprint-2		USN-12	As a user, I get email notifications at every stage: submitted, approved, assigned and closed.	2	Medium	Vamsi Bhavirisetti
Sprint-2		USN-13	As an admin, I can attach the workflow to the catalog item so every request follows the defined process.	2	High	Vamsi Bhavirisetti
Sprint-2	UI/UX development & customization	USN-14	As an employee, I can submit requests through a clean, easy-to-use catalog form.	2	Medium	Vamsi Bhavirisetti
Sprint-2		USN-15	As a user, I can follow a clear path from the catalog item to the REQ, RITM and approval status.	2	Medium	Vamsi Bhavirisetti
Sprint-2		USN-16	As a user, I can read tooltips and help text on form fields to fill them in easily.	1	Low	Vamsi Bhavirisetti
Sprint-2		USN-17	As an employee, I get mandatory-field checks and auto-fill from client scripts while completing the form.	3	High	Vamsi Bhavirisetti
Sprint-3	Data migration, testing & security	USN-18	As an admin, I can move existing car rental data into the new ServiceNow structure.	3	Medium	Vamsi Bhavirisetti
Sprint-3		USN-19	As an admin, I can enforce role-based access so only the right roles can view or approve requests.	3	High	Vamsi Bhavirisetti
Sprint-3		USN-20	As an admin, I can enforce data integrity so that no request moves ahead without the required approvals.	3	High	Vamsi Bhavirisetti
Sprint-3		USN-21	As a tester, I can run QA tests covering submission, approval routing, task creation and fulfillment.	5	High	Vamsi Bhavirisetti
Sprint-3		USN-22	As an admin, I can troubleshoot with flow execution logs and confirm that email notifications work.	3	Medium	Vamsi Bhavirisetti
Sprint-4	Deployment, documentation & final presentation	USN-23	As an admin, I can complete the Update Set, retrieve it on the target instance, preview it and commit it.	3	High	Vamsi Bhavirisetti
Sprint-4		USN-24	As a tester, I can verify the complete request flow on the target instance after deployment.	2	High	Vamsi Bhavirisetti
Sprint-4		USN-25	As a stakeholder, I can read the technical and user documentation for the solution.	3	Medium	Vamsi Bhavirisetti
Sprint-4	Project conclusion	USN-26	As a stakeholder, I can watch a final presentation and conclusion showing the working system.	2	Medium	Vamsi Bhavirisetti

Project Tracker, Velocity and Burndown Chart (4 Marks)


Sprint	Total story points	Duration	Sprint start date	Sprint end date (planned)	Story points completed (by planned end date)	Sprint release date (actual)
Sprint-1	16	6 days	26 Oct 2026	31 Oct 2026		
Sprint-2	20	6 days	02 Nov 2026	07 Nov 2026		
Sprint-3	17	6 days	09 Nov 2026	14 Nov 2026		
Sprint-4	10	6 days	16 Nov 2026	21 Nov 2026		

Velocity

The project runs for 4 sprints of 6 days each. Total story points = 16 + 20 + 17 + 10 = 63. Velocity = total story points ÷ number of sprints = 63 ÷ 4 = 15.75, roughly 16 story points per sprint. Average velocity per day = 16 ÷ 6 ≈ 2.67 story points per day.

Burndown Chart

A burndown chart shows the work remaining against time. The chart below gives the planned burndown of the 26 stories (63 story points) across the four sprints.

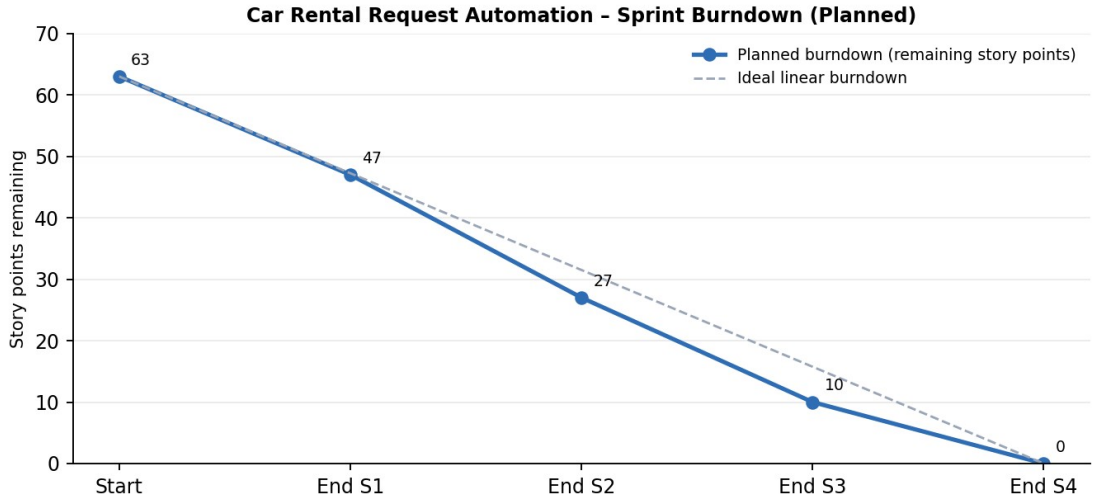

https://www.visual-paradigm.com/scrum/scrum-burndown-chart/

https://www.atlassian.com/agile/tutorials/burndown-charts

References

https://www.atlassian.com/agile/project-management

https://www.atlassian.com/agile/tutorials/how-to-do-scrum-with-jira-software

https://www.atlassian.com/agile/tutorials/epics

https://www.atlassian.com/agile/tutorials/sprints

https://www.atlassian.com/agile/project-management/estimation
